# SQA Workflow — Design to Sign-off

Oct 10, 2026 · @Spriha · Draft v0.1

QA is involved from the first approved design to the final sign-off note, so defects are prevented early rather than found late. This document describes how the team works today within our SDLC, and how each stage runs both without AI and with AI assistance.

## Purpose, scope and roles

**Scope:** every feature from approved Figma design and acceptance criteria (AC) through to QA sign-off. Production release and post-release monitoring are out of scope.

| Role | Responsibility in this workflow |
|---|---|
| Project Manager (PM) | Tracks timelines and progress across all projects and sprints; creates tickets ahead of sprint planning |
| Product Owner (PO) | Owns the ticket description and acceptance criteria; approves design; answers scope questions |
| Designer | Owns the Figma design; resolves UI questions raised by QA and Dev |
| Business Analyst (BA) | Clarifies business rules, edge cases and compliance needs |
| Developer | Builds the feature; deploys; comments the environment URL and test data; updates ticket status |
| QA Engineer | Reviews design and AC, writes test cases, executes tests, logs defects, retests, gives sign-off; checks the correct branch is deployed and deploys it through Jenkins when needed |
| QA Lead | Reviews test coverage and approves the sign-off note |

**Tools:** JIRA (tickets, bugs), Zephyr (test cases, test cycles, coverage), Figma (design), Confluence/Notion (test plans, sign-off notes), Postman (API testing), Jenkins (deployments). UI testing is manual; there is no UI automation.

## Sprint cadence

We follow Agile sprints: tickets are picked according to team capacity, and code freezes one week before release so that week is spent on regression testing of the release branch.

| Sprint event | When | QA's part |
|---|---|---|
| Ticket creation | Before sprint planning | PM creates the tickets in advance so sprint time is not lost to setup |
| Backlog grooming | Before the ticket enters a sprint | Stages 1 and 2: design and AC review, questions, risk, QA estimate |
| Sprint planning | Start of sprint | Team picks tickets according to capacity; QA effort is counted in that capacity |
| Daily stand-up | Every day | Testing progress, blockers, open defects |
| Development and testing | During the sprint | Stages 3 to 6: test design, handoff, execution, defects and retest |
| Mid-sprint meeting | Middle of the sprint | Team and PM check whether all tickets can still be completed in the sprint, so the burndown chart stays on track; QA flags testing at risk |
| Code freeze | One week before release | Release branch is cut; no new features merged, only PO-approved defect fixes |
| Regression week | The code freeze week | Stage 7: full regression on the release branch |
| Sprint review and retrospective | End of sprint | QA confirms what is tested and raises process issues |

| Sprint event | When | QA's part |
|---|---|---|
| Release | After regression week | Stage 8 sign-off note required before release |


## Scope changes during the sprint

A missing AC or new scope found during development or testing goes into a separate new ticket; the original ticket is never changed once work has started.

- Applies to tickets in progress, tickets already passed to QA, and tickets marked Done.
- The new ticket is created (usually by the PM), linked to the original, and tracked on its own through this same workflow, with its own test cases linked to it.
- QA tests the original ticket against its original AC only; the new scope is tested under the new ticket.
- A missing AC found during testing is raised as a new ticket, not logged as a bug on the original.

| Activity | Without AI | With AI |
|---|---|---|
| Raise the gap | QA or Dev describes the missing AC or scope in the team channel or ticket comment | Same |
| Create the new ticket | PM writes the ticket and links it to the original | AI drafts the ticket description and proposed AC from the discussion; PM and PO review before saving |
| Plan it | Team decides whether it fits this sprint's capacity or goes to the backlog | Same |

# Workflow at a glance

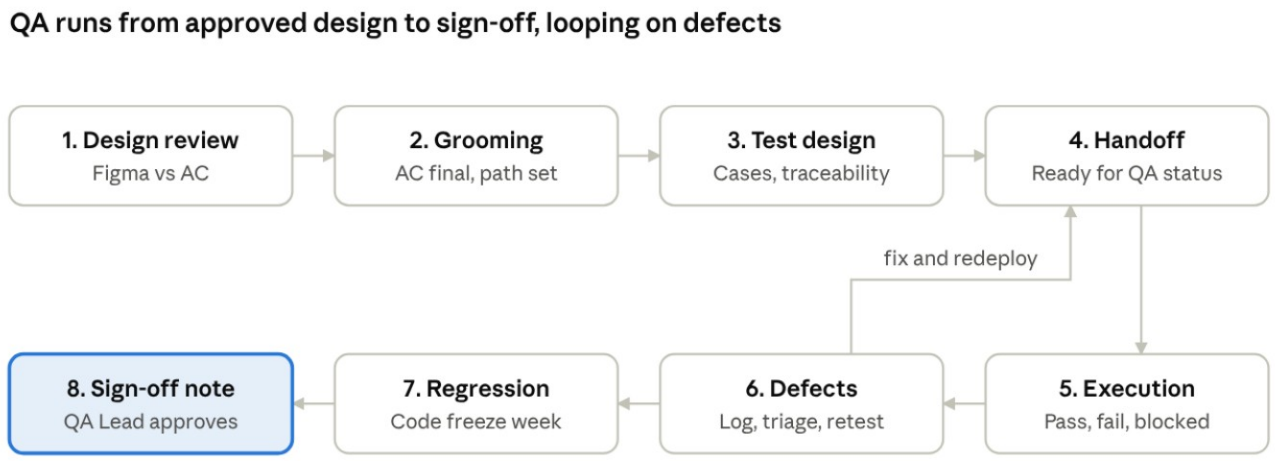


SQA workflow · 8 stages, 1 defect loop

Stages 1 to 3 run before and during development; a failed retest loops back through the handoff until the defect is fixed, and only then does the feature move to regression and sign-off.

## Stage 1: Figma design and acceptance criteria review

QA reviews the approved Figma design against the AC before grooming, so gaps are raised while they are still cheap to fix.

**Entry:** Figma design approved by PO; ticket has a description and AC written by the PO.

| Activity | Without AI | With AI |
|---|---|---|
| Understand the feature | Read the ticket, AC and every Figma screen manually | AI summarises the ticket and AC into a one-page feature brief; QA verifies it against Figma |
| Check design vs AC | Walk each screen and match it to each AC line by hand | AI lists AC lines with no matching screen or state, and screens with no AC; QA confirms each item |
| Find missing states | QA lists empty, error, loading, disabled and permission states from experience | AI suggests missing states and edge cases per screen; QA keeps only the relevant ones |

| Activity | Without AI | With AI |
|---|---|---|
| Check testability | QA flags vague AC wording such as "fast" or "user-friendly" | AI flags ambiguous or untestable AC lines and proposes measurable wording |
| Record questions | QA writes questions in the ticket or a shared doc | AI drafts the question list; QA edits it before posting |

**Exit / output:** a list of design and AC questions attached to the ticket, ready for grooming.

## Stage 2: Backlog grooming

In grooming, QA brings the Stage 1 questions so the team agrees on scope, AC and risk before estimation.

**Entry:** Stage 1 question list ready; PO, Designer, BA, Dev and QA attend.

| Activity | Without AI | With AI |
|---|---|---|
| Walk through the feature | PO presents the ticket and Figma; QA raises questions one by one | Same, with the AI feature brief shared in advance so the session starts with questions, not reading |
| Clarify AC | Team agrees answers; PO updates AC in the ticket | AI drafts revised AC from the meeting notes; PO reviews and updates the ticket |
| Assess risk | QA and Dev judge impact on existing flows, roles, data and compliance | AI lists modules and flows likely affected; team confirms the real impact |
| Estimate QA effort | QA estimates from past similar tickets | AI suggests an estimate based on test case count and complexity; QA adjusts |
| Choose QA path | Team agrees Pilot QA (default) or Dev QA (high-risk changes only) | Same; the decision stays with the team |
| Capture notes | QA writes meeting notes manually | AI produces meeting notes and action items; QA checks and posts them |

**Exit / output:** AC finalised by the PO, open questions resolved or assigned, QA estimate and QA path agreed, ticket marked ready for sprint.

## Stage 3: Test planning and test case design

While development is in progress, QA writes the test cases so testing can start the moment the build is handed over.

**Entry:** ticket picked in sprint planning according to team capacity, with final AC.

| Activity | Without AI | With AI |
|---|---|---|
| Test scope | QA lists in-scope and out-of-scope items, roles and environments | AI drafts the scope from the ticket and grooming notes; QA corrects it |
| Test scenarios | QA derives scenarios from each AC line | AI generates scenarios per AC line; QA removes duplicates and adds business context |
| Test cases | QA writes test cases in Zephyr with steps, test data and expected results | AI drafts test cases in the Zephyr format; QA reviews every step and expected result |
| Negative, boundary and validation cases | QA applies boundary value analysis and equivalence partitioning by hand | AI proposes boundary, invalid input and role-permission cases; QA confirms against business rules |
| API tests | QA builds Postman requests and collections from the API spec | AI drafts Postman requests and assertions from the spec; QA runs and fixes them |
| Traceability | QA links each Zephyr test case to the JIRA story and maps it to an AC line | AI builds the AC-to-test-case matrix and flags uncovered AC lines |
| Peer review | QA Lead or a peer reviews the test cases | Same; AI can do a first-pass review for gaps before the human review |

**Exit / output:** reviewed test cases in Zephyr, linked to the JIRA ticket, test data identified, AC-to-test-case traceability complete.

## Stage 4: Dev-to-QA handoff

A build reaches QA only through the handoff SOP: the developer deploys, comments the environment details, and moves the ticket to the agreed QA status. QA then checks in Jenkins that the correct branch is deployed, and deploys it themselves if it is not.

**Entry:** development complete and deployed.

| Activity | Without AI | With AI |
|---|---|---|
| Deploy | Developer deploys to Pilot (default) or Dev (high-risk only) | Same |
| Handoff comment | Developer adds the environment URL and test data in a ticket comment | Same; AI can check the comment and flag a missing URL or test data |
| Status update | Developer moves the ticket to "Ready for Pilot QA" or "Ready for Dev QA" | Same |
| Verify deployed branch | QA checks in Jenkins that the correct branch is deployed to the environment | Same |
| Deploy if needed | If the correct branch is not deployed, QA deploys it through Jenkins | Same |
| Smoke check | QA opens the build and checks the feature loads and the main flow works | Same; a Postman smoke collection can check the main APIs first |
| Reject incomplete handoff | QA returns the ticket if the URL, test data or build is missing or broken | Same |

**Exit / output:** build accepted by QA, ticket in a Ready for QA status.

## Stage 5: Test execution

QA runs every planned test case on the handed-over build and records a pass, fail or blocked result with evidence.

**Entry:** build accepted in Stage 4; reviewed test cases ready.

| Activity | Without AI | With AI |
|---|---|---|
| Create test cycle | QA creates a Zephyr test cycle for the ticket and adds its test cases | Same |
| Functional UI testing | QA executes each test case in the cycle manually across all user roles | Same; AI is not a substitute for hands-on execution |
| API testing | QA runs Postman collections and checks responses, status codes and data | Same; AI helps read failed responses and suggests likely causes |
| Design check | QA compares screens to Figma by eye | AI-assisted visual comparison highlights differences; QA judges which matter |
| Exploratory testing | QA explores beyond the test cases using experience | AI suggests exploratory charters and risky areas; QA explores |
| Audit trail and data checks | QA verifies audit trails, data integrity and transaction accuracy | Same; never delegated to AI |
| Record results | QA marks each test case Pass, Fail or Blocked in the cycle and attaches evidence | Same; QA records every result |
| Track coverage | QA reads executed vs total test cases from the cycle | AI turns the cycle's numbers into a daily status update; QA verifies them |

**Exit / output:** every test case in the Zephyr cycle has a result; coverage is read from the cycle; failures are logged as JIRA bugs and linked to the failed test cases.

## Stage 6: Defect management and retest

Every failure becomes a JIRA defect with clear steps and evidence, and loops back to the developer until it passes retest.

**Entry:** at least one failed test case from Stage 5.

| Activity | Without AI | With AI |
|---|---|---|
| Log defect | QA logs a JIRA bug with title, steps, expected vs actual, environment, role and evidence, and links it to the failed Zephyr test case | AI drafts the defect from QA's notes and screenshots; QA checks every field and links the bug to the failed test case |
| Severity and priority | QA sets severity; PO confirms priority | AI suggests severity from impact; QA and PO decide |
| Duplicate check | QA searches JIRA for similar defects | AI finds likely duplicates; QA confirms |
| Triage | QA, Dev and PO agree fix, defer or reject | Same |
| Fix and redeploy | Developer fixes, redeploys and comments per the handoff SOP | Same |
| Retest | QA re-executes the linked test case in the Zephyr cycle, then closes or reopens the bug | Same |
| Impact retest | QA retests related test cases around the fix | AI suggests which related cases are most likely affected; QA decides |

**Exit / output:** all critical and high defects closed; any remaining defects deferred with PO approval.

## Stage 7: Code freeze and regression week

Code freezes one week before release, and QA spends that week running regression on the release branch so no sprint change breaks existing flows.

**Entry:** Stage 6 exit met for every ticket in the release; release branch cut, and QA has confirmed in Jenkins that the release branch is deployed (deploying it if not).

| Activity | Without AI | With AI |
|---|---|---|
| Code freeze | Release branch cut one week before release; after that only PO-approved defect fixes are merged | Same |
| Select regression scope | QA picks regression cases covering every ticket in the release plus core flows | AI ranks regression cases by the areas the release's tickets touch; QA finalises the list |
| Run regression on release branch | QA creates a regression test cycle in Zephyr and runs manual regression and the Postman API collections on the release branch build | Same; AI helps read failed API responses |
| Freeze-week defects | QA logs and triages; a fix is merged to the release branch only if approved, then retested | AI drafts defect reports; QA checks every field |
| UAT support | QA walks the PO through the release against the AC | AI prepares a UAT checklist from the AC; QA walks the PO through it |
| Final retest | QA reruns cases affected by fixes merged during the freeze | AI suggests which cases those fixes affect; QA decides |

**Exit / output:** regression passed on the release branch, PO has accepted the release against the AC.

## Stage 8: QA sign-off note

QA issues a written sign-off note once all exit criteria are met; the QA Lead approves it and the PO receives it as the record that the feature is ready for release.

**Sign-off criteria:**

- [ ] All planned test cases executed
- [ ] No open critical or high defects

- [ ] Remaining defects deferred with PO approval and listed in the note
- [ ] Regression passed
- [ ] All Zephyr test cases linked to the JIRA ticket, and every AC line traced to at least one passed test case
- [ ] PO acceptance received

**Sign-off note contents:**

| Section | What it contains |
|---|---|
| Feature | Ticket ID, feature name, sprint, release |
| Environment | Pilot or Dev, build version, test dates |
| Scope tested | Modules, user roles, browsers or devices covered |
| Out of scope | What was not tested and why |
| Results | Test cases total, passed, failed, blocked; Postman API test results |
| Defects | Total raised, closed, deferred, with IDs of deferred ones |
| Known issues and risks | Anything the release team or PO should know |
| Recommendation | Go, or Go with known issues |
| Approval | QA Engineer, QA Lead, PO names and dates |

| Activity | Without AI | With AI |
|---|---|---|
| Compile results | QA takes execution counts and coverage from the Zephyr test cycles and bug counts from JIRA | AI compiles counts and defect lists into the template; QA verifies each number against Zephyr and JIRA |
| Write the note | QA writes the summary, risks and recommendation | AI drafts the summary and risk section; QA rewrites as needed and owns the recommendation |
| Approve and share | QA Lead approves; note posted in Confluence and linked on the ticket | Same |

# With vs without AI: summary and guardrails

The stages, owners and sign-off criteria are the same in both processes; AI speeds up drafting and analysis, while QA keeps every decision and every test verdict.

| Aspect | Without AI | With AI |
|---|---|---|
| Who decides | QA, PO, Dev | QA, PO, Dev (unchanged) |
| Where time goes | Writing test cases, defects, notes and reports | Reviewing and correcting AI drafts; more time for exploratory and risk-based testing |
| Coverage gaps | Depend on individual experience | AI suggests extra edge cases; QA filters them |
| Main risk | Missed cases under time pressure | Trusting an AI draft without checking it |

**Guardrails when using AI:**

1. Never paste real customer data, account numbers, credentials or production data into an AI tool; use masked or synthetic test data only.
2. Use only company-approved AI tools.
3. QA reviews every AI-generated test case, defect, script and report before it is saved or shared.
4. AI never marks a test as passed; only a human execution result counts.
5. Audit trail, compliance and transaction-integrity checks are always done by QA directly.
6. Every number in the sign-off note is checked against Zephyr and JIRA before approval.
